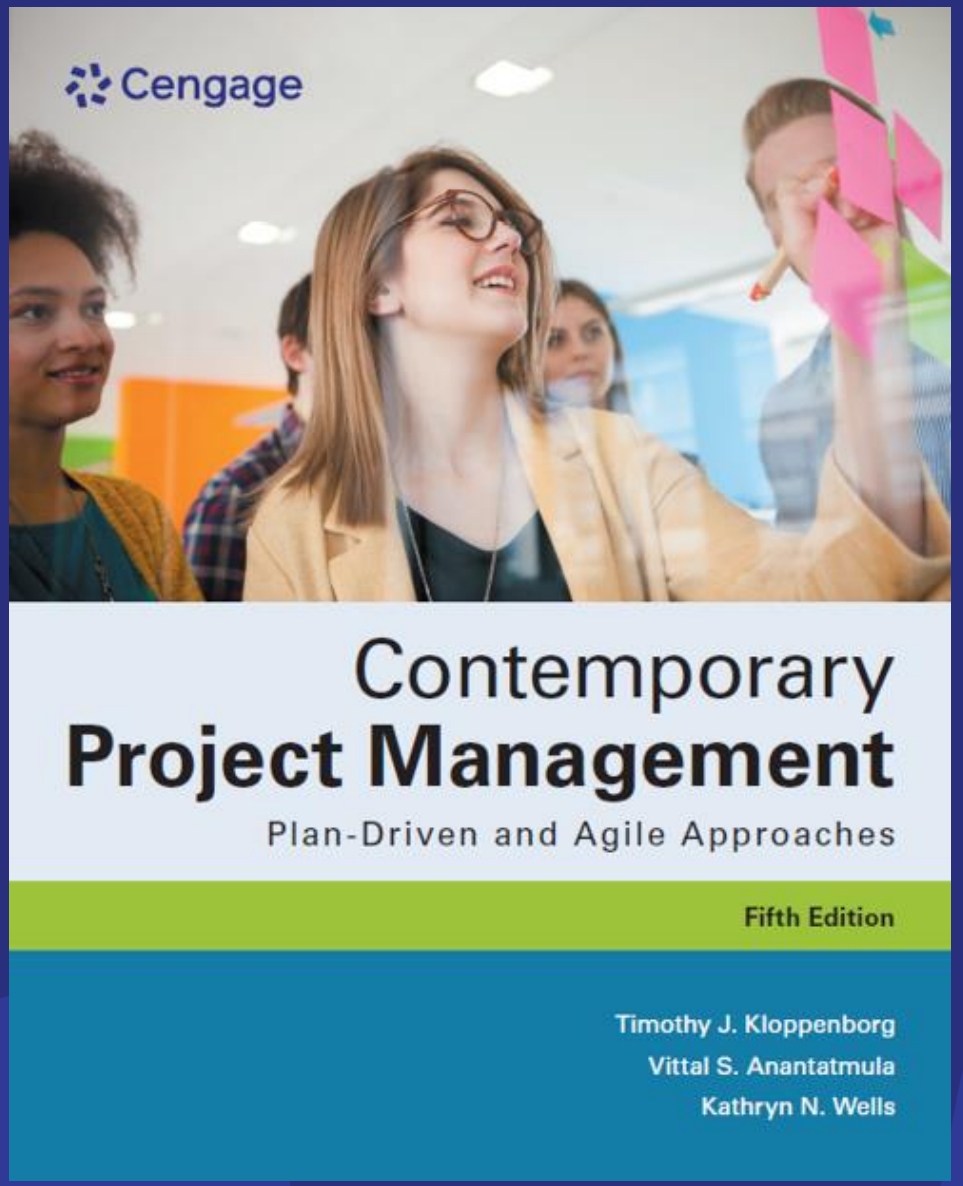


Chapter 15


Finishing the Project and Realizing the Benefits

Cengage

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.


Icebreaker

What are two things you learned from Determining Project Progress and Results?

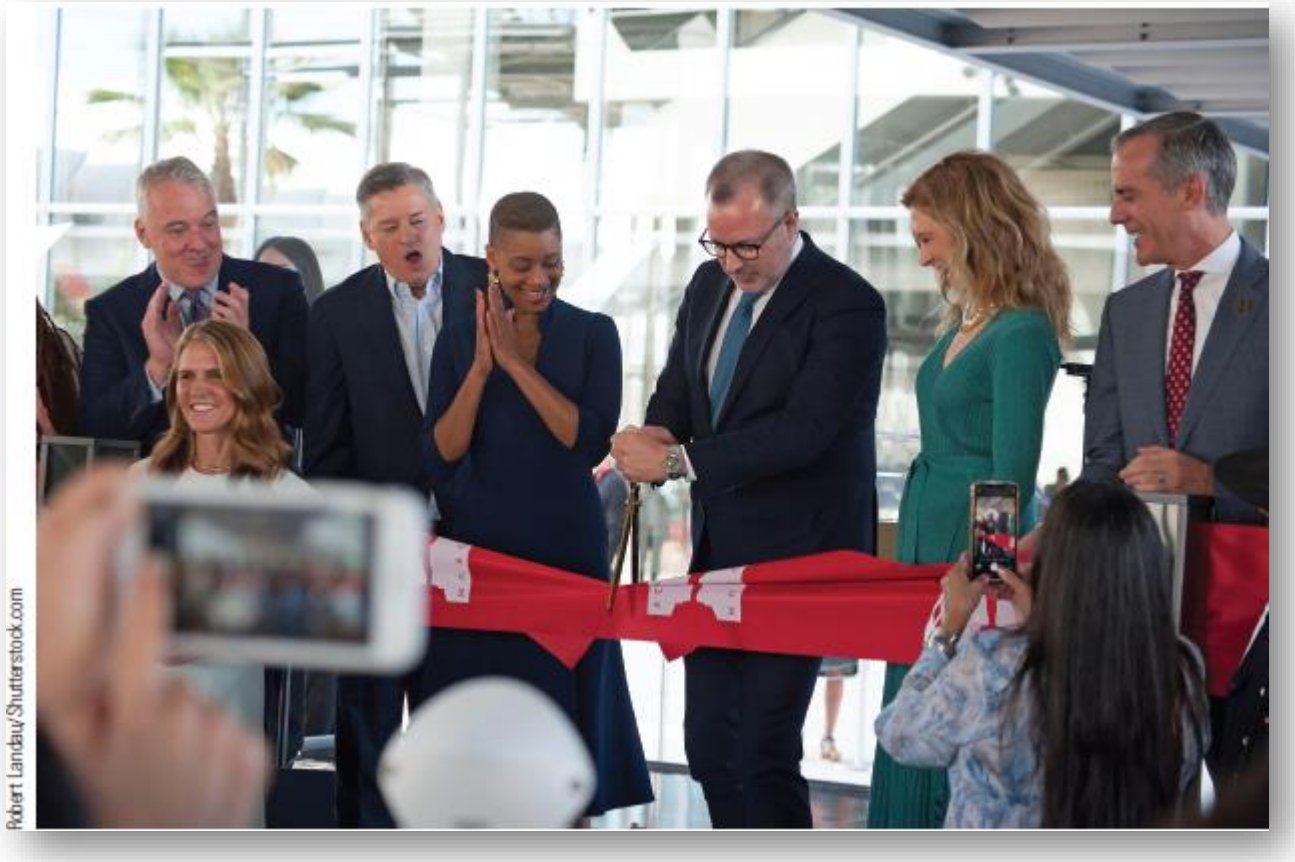

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Finishing the Project and Realizing the Benefits (1 of 2)

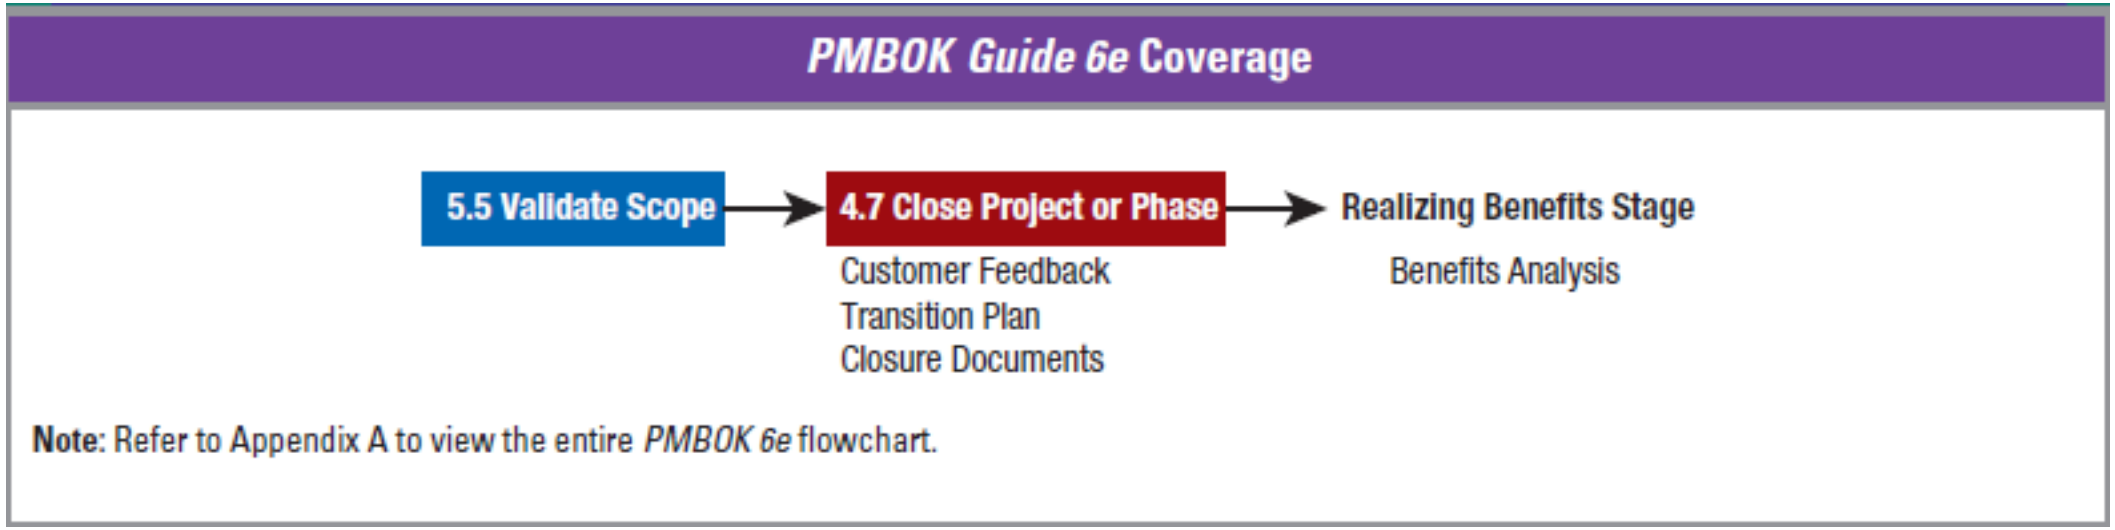

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Core Objectives

- **15-1** Summarize how to determine when a project should be terminated early.
- **15-2** Describe the process for terminating a project in normal completion time.
- **15-3** Justify the importance of the project closing activities.
- **15-4** Create and present a transition plan for the project, including a plan for ongoing support and sharing lessons learned.
- **15-5** Capture, document, and share project lessons learned.
- **15-6** Secure customer feedback and acceptance of the project.
- **15-7** Close your projects administratively and technically.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Agile Objective

- **15-8** Describe processes associated with capturing and using knowledge gained from Agile projects (if your team was to move together onto a new project).

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Finishing the Project and Realizing the Benefits (2 of 2)

Overview of the Book
15.1 Validate Scope
15.2 Terminate Projects Early
15.3 Close Project
15.4 Post-Project Activities
15.5 *PMBOK Guide 7e*
15.6 Agile Projects
15.7 Using MS Project for Project Closure
Summary

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.1 Validate Scope (1 of 2)

Validate Scope
Punch List

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.1 Validate Scope (2 of 2)

- Formal acceptance of completed project deliverables.
- Buyer provides the seller with formal written acceptance.
- Transition from executing stage to closing stage.
- Use a project closeout checklist to itemize project activities and/or deliverables.

Validate scope—formally accepting the completed project deliverables

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Punch List

Punch List is the list of "*work items that are identified during a final inspection that need to be completed*."

- Project managers need to ensure that all the project work has been successfully completed.
- They can refer to the charter, scope statement, WBS, schedule, and all communications plans to verify that everything they committed to do is complete.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Exhibit 15.1

Example Project Closeout Checklist

Project Name: Closeout Date:

Project Team:

Project Manager:
Sponsor:

Item	Who	Target Date	Completion Date
Final Certificate of Occupancy			
Punch List Complete			
Notice of Punch List Completion			
Certificate of Substantial Completion			
Utilities Transferred to Owner			
Notice to Owner on Insurance			
Facility Manual			
As-Built Drawings			
Attach Job Files to Database			
Update Projects Database			
Final Retainage Billing			
Release of Subcontractor Retainage			
Complete Subcontractor Evaluations			
Team Close-Out Meeting			
Send Out Owner Survey			
Bond Release			
Estimating Feedback Cost Report			

Approved for Closeout:

Project Manager _____ Sponsor _____ Vice President–Construction _____

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.2 Terminate Projects Early

Mutual Agreements
Terminations for Default
Terminations for Convenience of Buyer

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Mutual Agreements

Remaining deliverables need to be integrated into another project, stopped altogether, or continued as a lesser project or a further phase of the final project.

If agreement cannot be reached by direct negotiations, either legal or alternative dispute resolution methods can be used to reach a settlement.

It is in the best interest of all parties to finish the project as is and part as friends.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Termination for Default

Terminations for default occur for projects executed externally and often result from a problem with the project's cost, schedule, or performance.

A buyer can also decide to terminate a project early because they have lost confidence in the contractor performing the project.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Termination for Convenience of Buyer

Projects can be cancelled for the convenience of the buyer.

If a customer decides to terminate a project for convenience, it invokes a contract clause.

This clause normally stipulates that the contractor is reimbursed for the money it has spent up to that point and the customer takes ownership of the deliverables in whatever form they currently exist.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.3 Close Project

15.3a Write Transition Plan
15.3b Knowledge Management
15.3c Create the Closeout Report

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.3a Write Transition Plan

A **Transition Plan** helps the customer use the project deliverables successfully.

The reason a project is performed is that some person or organization needs the resulting deliverables.

A Transition Plan helps to ensure the following:

- Quality problems are avoided during the transition.
- The project deliverables move into their service or operational role.
- The needed maintenance, upgrades, and training take place.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.


15.3b Capture Lessons Learned

Lessons Learned:

- are the useful knowledge gained by project team members as they perform a project and the results that transpired.
- can include what worked well that the project team members think should be copied and/or adapted for use on future work.
- can also include areas for which a different method may yield better results. Information about mistakes and what went wrong should be captured to avoid repeating them again.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Exhibit 15.2

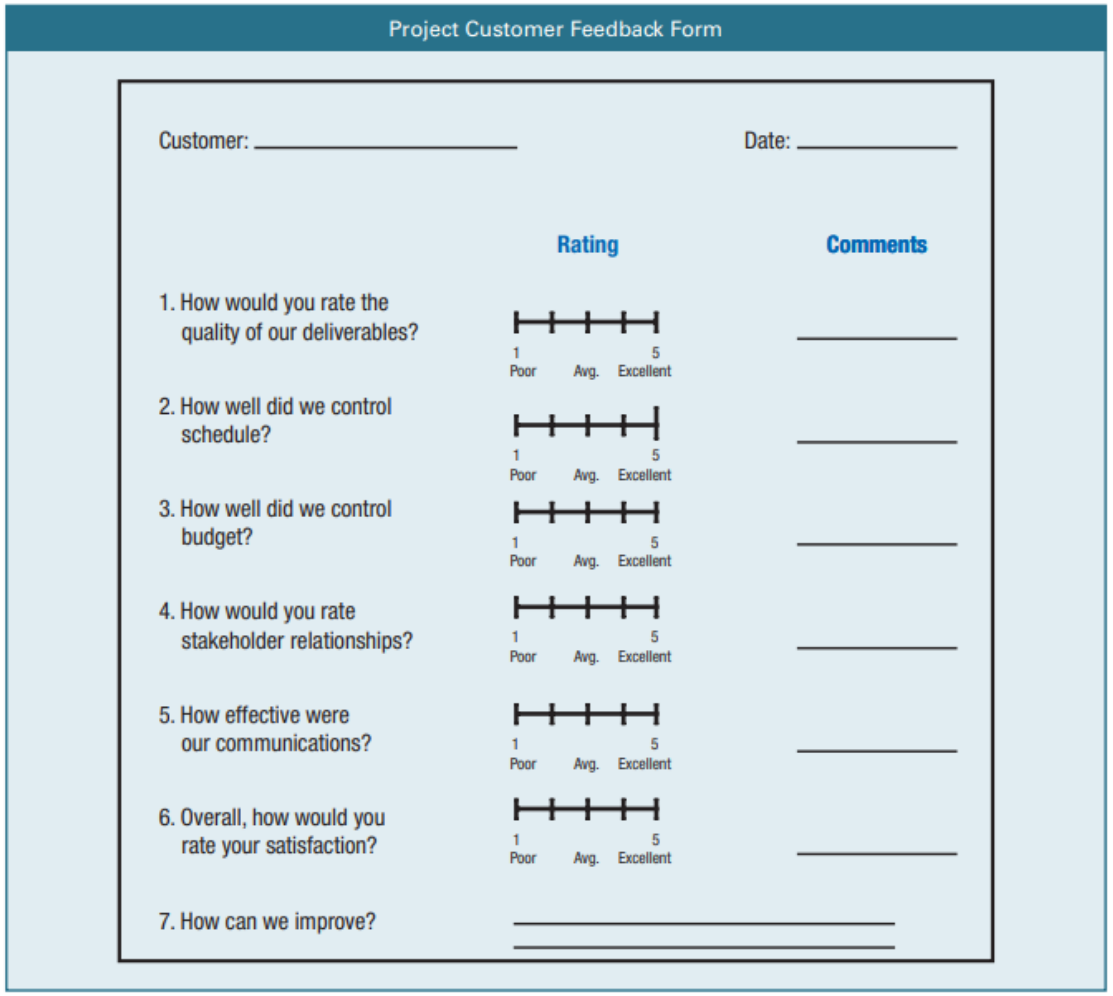

Project Customer Feedback Form

Customer: _____ Date: _____

	Rating	Comments
1. How would you rate the quality of our deliverables?	1 Poor Avg. 5 Excellent	_____
2. How well did we control schedule?	1 Poor Avg. 5 Excellent	_____
3. How well did we control budget?	1 Poor Avg. 5 Excellent	_____
4. How would you rate stakeholder relationships?	1 Poor Avg. 5 Excellent	_____
5. How effective were our communications?	1 Poor Avg. 5 Excellent	_____
6. Overall, how would you rate your satisfaction?	1 Poor Avg. 5 Excellent	_____
7. How can we improve?	_____ _____	

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Exhibit 15.3

Lessons-Learned Project Closing Document

D.D.Williamson
World Leader in Caramel Color

Project Number:
Closing Date:

PROJECT CLOSING DOCUMENT:

As your project comes to a close, please capture continuous improvements, lessons learned and issues to consider for future projects. Please focus on the positive aspects that would help other teams in the future and you would like to see done again (+) and on things that could be changed/improved upon in the future (Δ). These learnings will be entered into a database for future reference to help all associates.

Criteria	Plan	Actual	Learnings (+/Δ)
Outcome • Future state achieved? • Success measure (attach graph/data)			
Schedule • Milestones • Completion			
Cost (Cap Ex)			
Hours required: • Project Manager • Sponsor • Core team members • SMEs			

Risks and Countermeasures	
Anticipated	Unanticipated

Communication Plan Implementation	
What worked well (+)	What did not work (Δ)

Other Learnings	
What worked well (+)	What did not work (Δ)

Source: Elaine Gravatte, D. D. Williamson.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Disseminate and Use Lessons Learned

- The process of capturing and discussing lessons learned is valuable learning for the participants.
- More organizations effectively collect lessons learned than effectively disseminate and use them.
- Some organizations have created databases, shared folders, or wikis for this purpose.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Exhibit 15.4 (1 of 2)

Lessons-Learned Example

Accountability:	Use formal accountability and measurement systems down to the individual performance level. Ensure all team members have clearly defined roles and responsibilities.
Buy-In And Commitment:	It is helpful when directors attend project meetings. Be sure sponsor secures buy-in from other executives. Involve people with decision-making authority early in the project.
Communication:	Develop and follow a communications management plan to develop trust. Communication about change needs to be ongoing. Communication needs to be early and ongoing with all key audiences and stakeholders.
Complexity:	Many projects are multifaceted and involve numerous trade-offs that need to be managed. Project manager should attend some client meetings and sponsor should attend some team meetings to ensure integration.
Culture and Change:	Lean concepts challenge the organization's culture for data collection and transparency. Commitment to transparency and change is needed prior to project initiation. Educating leaders in change management strategies helps them deal with resistance.
Expectations:	Set and state clear expectations. Define and stay within scope. Manage expectations of sponsor, stakeholders, customers, and project team.
Meetings:	Team members should be prepared with previous meeting minutes, agenda, and project updates. End a meeting with clear action items and due dates for each team member. Plan meetings in advance to make them more efficient.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Exhibit 15.4 (2 of 2)

Planning:	Have well-defined roles and responsibilities. Scale planning at the appropriate level of detail. Expect many revisions.
Process Improvement:	Always discuss what we could have done better. Keep working to sustain results on completed projects. Investigate feedback provided to assure it is understood and utilized as appropriate.
Project Team:	Listen to and respect input from all team members. Let each team member be responsible for setting their own timetable to the extent possible. Determine in advance how the project team will make decisions.
Scope:	Define success early. Be specific about scope. Manage scope creep.
Sponsor Support:	Sponsors and other leaders need to publicly endorse the project and remove barriers. Speak candidly and informally to your sponsor in addition to formal reports. Obtain sponsor's signature on charter before proceeding.
Stakeholders:	Invite key stakeholders to specific meetings. Be sensitive to the political climate within your client's organization. Be open to constructive criticism and other input from stakeholders.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.3c Create the Closeout Report

- The Closeout Report usually includes a **summary status** of the project that can be gleaned from progress reports.
- The Closeout Report also normally includes **lessons learned** and often contains a review of the project's original justification.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Exhibit 15.5

Closeout Report Template

This deliverable, required for each small project, contains the project charter, the original work breakdown structure, summary of weekly progress reports, and client feedback summary.

Project Summary Report for Project _____

Task or Item Description	Satisfactory	Unsatisfactory	Comments
A. Project charter updated and included			
B. Original WBS included			
C. Weekly progress report summary included			
D. Client feedback summary included			

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Exhibit 15.6

Project Team Transition to New Project

Congratulations! You and your team have successfully completed the project. Now, how can your team best transition to the next project?

Know that "[s]trengths-based project teams integrate their knowledge, skills, and practice of strengths development with project management tools and techniques, equipping the project team to **apply** and maximize their collective strengths to successfully complete their project on time, within budget, and according to the project objectives and specifications."[1] Therefore, an experienced strengths-based project team knows how to work together, considers the tasks in front of them, and leverages their strengths toward successfully completing their project. At the end of each project, it is critical that the project team captures their collective team strengths and how they effectively applied those strengths on their project.

Before starting the next project, consider this four-step process, then complete the following action plan template:

1. **Review:** Document what the team has, including their strengths (talents, skills, knowledge, areas of expertise) and project management tools. Capture what has "worked" for the team as they successfully completed their previous projects.
2. **Identify:** Look at the team's upcoming project challenges (or major tasks).
3. **Articulate:** Select the best project management tools, techniques, and strengths to use toward the challenges/major tasks.
4. **Create:** Develop an action plan for applying and tracking the project team's collective strengths.

CHALLENGE TRACKING – Action Plan Template

Applying your Project Team's Collective Strengths

Describe the new challenge (or major task) facing the project team.	**What collective strengths from the team could you apply?**	**What are the expected results?**	**What support does the team need from the customer or sponsor?**

So hit the ground running on your next project in just four steps: Review, Identify, Articulate, and Create an Action Plan. Strengths-based project teams finish the project strong and start the next project even stronger!

Source: Martha Buelt, MA and Connie Plowman, PMP, authors of *Developing Strengths-Based Project Teams*.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.4 Post-Project Activities

15.4a Reassign Workers
15.4b Celebrate Success and Reward Participants
15.4c Provide Ongoing Support
15.4d Ensure Project Benefits Are Realized

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.4a Reassign Workers

- Helping good workers secure follow-on work is one of the most important things a project manager must do toward the end of a project.
- It is important to understand aspirations and recognize individual strengths of all the project team members to make recommendations for future project assignments.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.4b Celebrate Success and Reward Participants

Challenge

Energize

Limit

Exert

Believe

Recognize **A**cknowledge **T**ransition

Ease Stress



Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.4c Provide Ongoing Support

- A **Transition Plan** can guide ongoing support in the forms of training, change management, and/or other services.
- Project managers aim to create useful project deliverables on time and on budget.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.4d Ensure Project Benefits are Realized

- Many organizations insist that project managers follow up with customers weeks or months after the project deliverables are in place.
- One of the most important measures of project success is how well the customers can use the project deliverables.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.5 *PMBOK Guide 7e*

15.5a Stakeholders
15.5b Team
15.5c Development Approach & Lifecycle/Delivery

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.5a Stakeholders

- PMI makes clear that the goal of project management is to provide value to stakeholders.
- We may do this through deliverables, but the desired outcome is not the deliverables themselves but rather the value and benefits they afford our stakeholders.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.5b Team

- Team members should be recognized for their work and any professional growth they have experienced through their time on the project.
- Lessons learned can refer to both tacit and explicit knowledge and should be captured in such a way that future teams can look back to them for guidance.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.5c Development Approach & Lifecycle/Delivery

- In an **adaptive lifecycle**, it is ultimately up to the product owner to decide when we have gone as far as is necessary, based on the “definition of done.”
- If we have been using more of a **predictive approach**, we may not have much to deliver until near the end of the project.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.6 Agile Projects

- Scope needs to be validated on any project so the customer can formally accept the deliverables and state their satisfaction.
- On Agile projects, scope is validated at every iteration and release when the team demonstrates to the customer how the items they produced work.
- This frequent and early direct feedback from customers and other stakeholders improves solutions and increases customer satisfaction.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Exhibit 15.7

Comparison of Plan-Driven and Agile Approaches for Finishing the Project and Realizing Benefits

Finishing the Project and Realizing Benefits Questions	Plan-Driven	Agile
When is scope validated?	At the end of the project or phase	In demonstrations at the end of iterations and releases
How do you terminate a project early?	By mutual agreement, default, or convenience of buyer	Product Owner pivots using money for nothing or change for free contract clauses
How is knowledge management handled?	Lessons learned are captured at the end of a phase or project and added to a repository	Retrospectives are conducted at the end of every iteration
What happens to team members at the end of the project?	They are individually reassigned or disbanded	The team is reassigned as a unit
How is ongoing support handled?	Through a transition plan	Through a transition plan

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.7 Using MS Project for Project Closure

15.7a Creating Project Progress Reports
15.7b Archiving Project Work

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.7a Creating Project Progress Reports

Three ways to create MS Project Reports:

1. Create a customizable canned report.
2. Sharing reports.
3. Export a report to MS Excel.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.


Create a Customizable Canned Report

1. Click the **Report Tab>>View Reports Group>>Dashboards>>Project Overview**

(Note: Once generated, the elements of the report can be manipulated and customized. Element position can be changed by clicking and dragging to different areas of the report, and fonts, colors, shading, and effects can be altered by double-clicking elements to open formatting panels.)


Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Exhibit 15.8

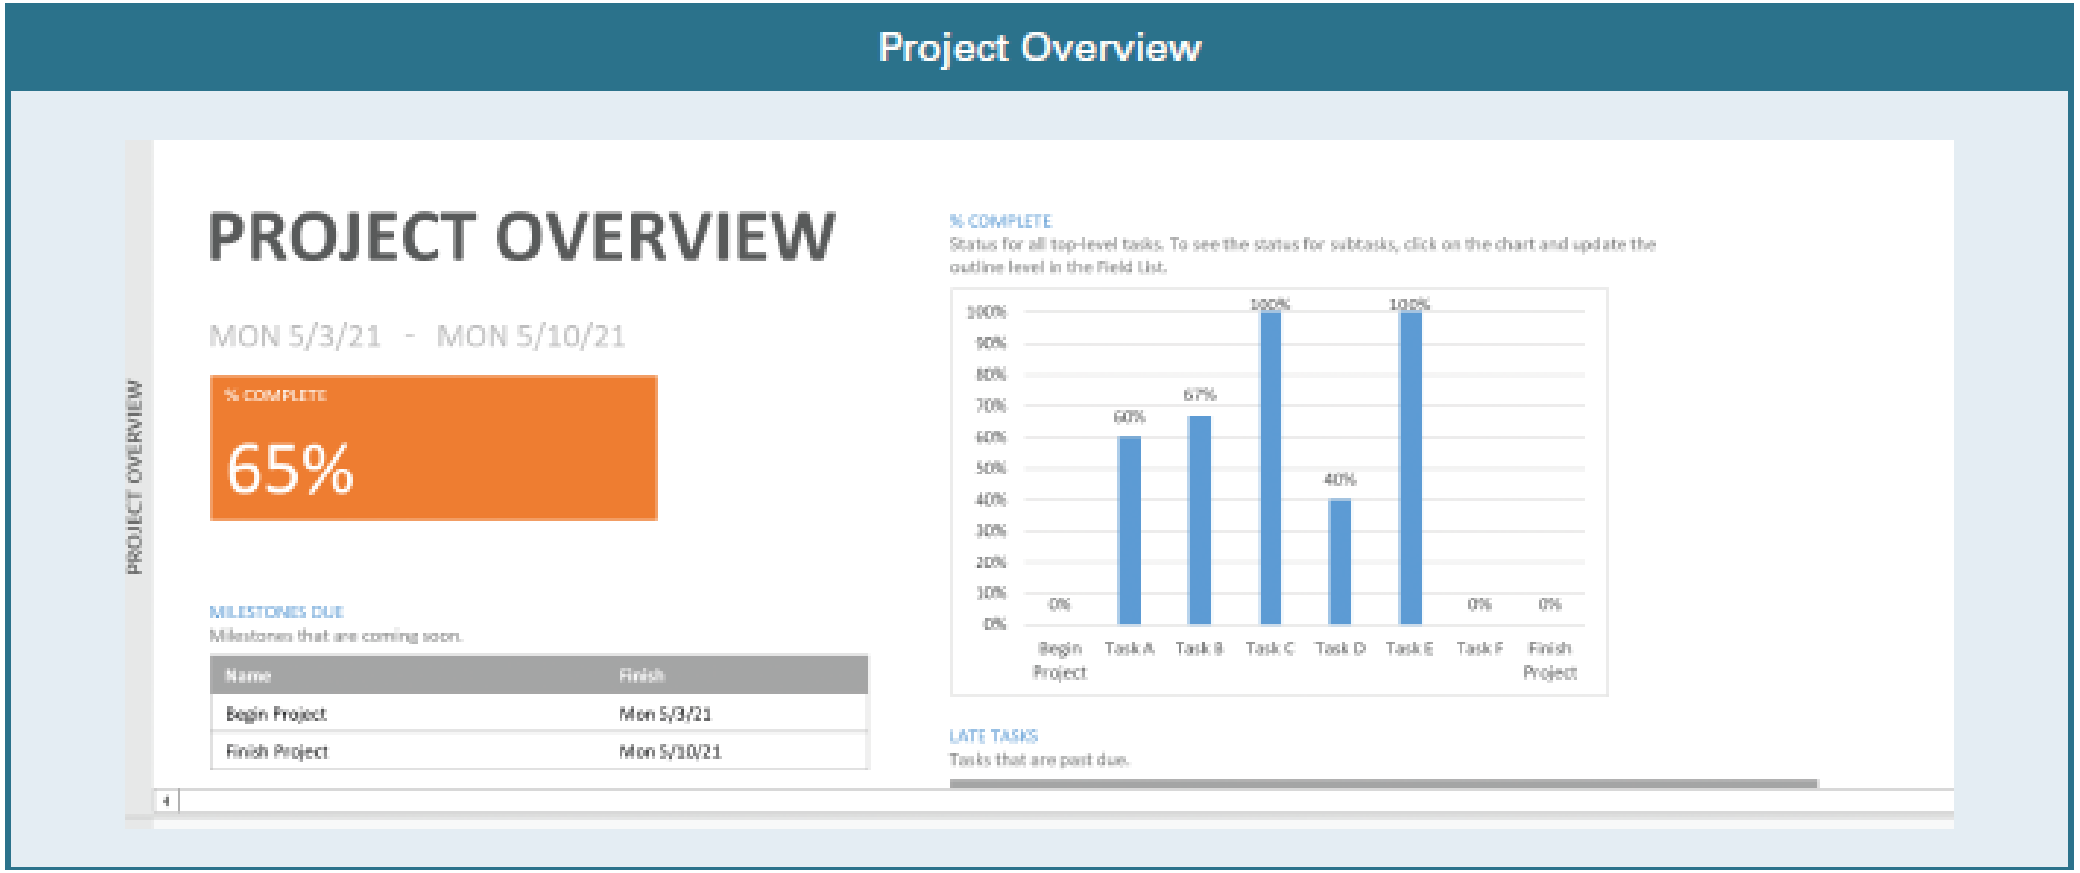

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Exhibit 15.9

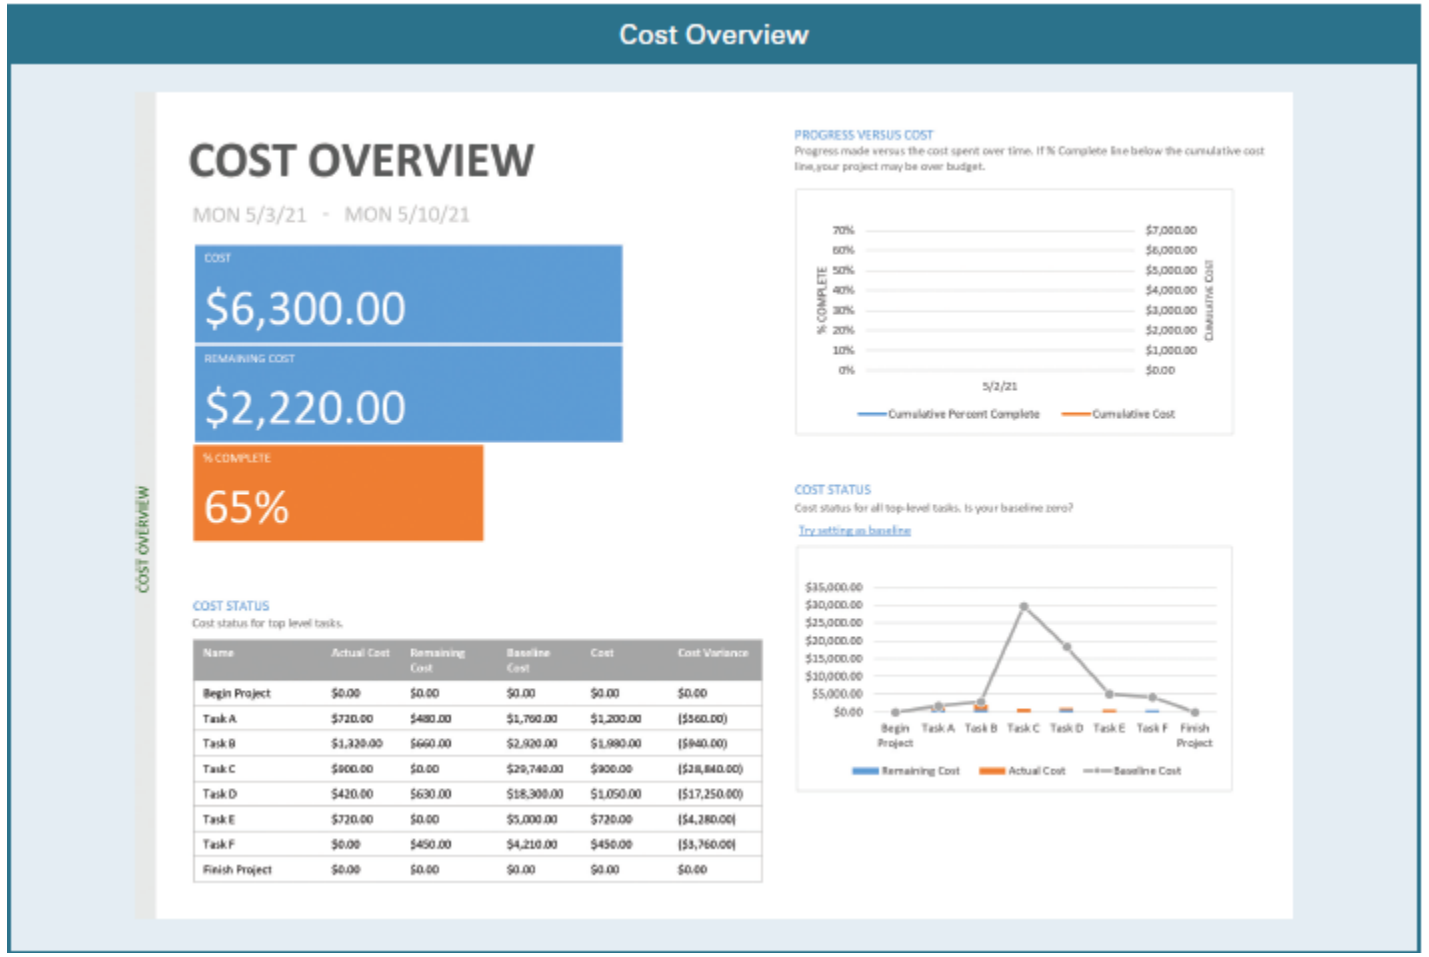

Cengage

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage. All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Sharing Reports

- Once the report is formatted to your specification, it can be printed or saved as a PDF and published to e-mail, a web portal, or other location.
- MS Project has native support for sharing to e-mail or MS SharePoint in the File>>Share menu options.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.


Export a Report to MS Excel

1. Click the **Report Tab**>>**Export Group** >>**Visual Reports**.
2. Click the **Resource Summary Tab**>> select **Resource Remaining Work Report.**
3. Click **View**.
4. The report will build and then open in MS Excel *(where it can be customized and distributed)*.
5. Click **Close** to close the Visual Reports dialog *(Exhibit 15.12)* in MS Project.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.


Exhibit 15.11

Resources Remaining Work Report

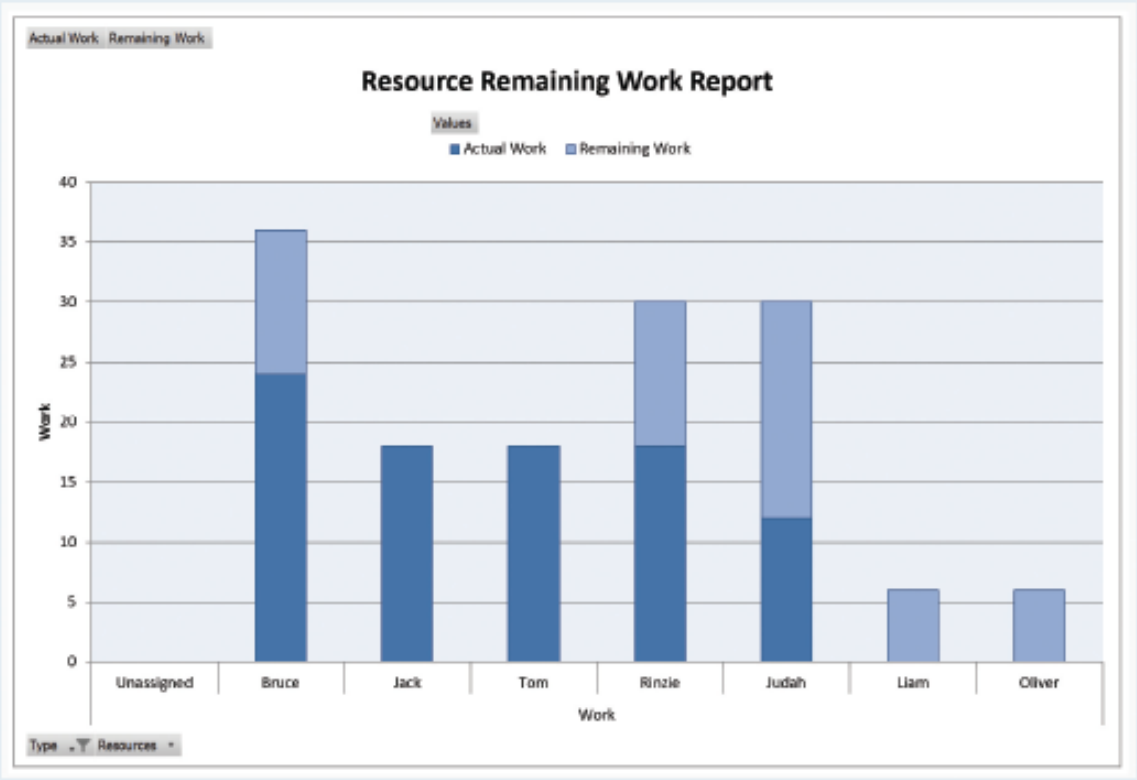

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Exhibit 15.12

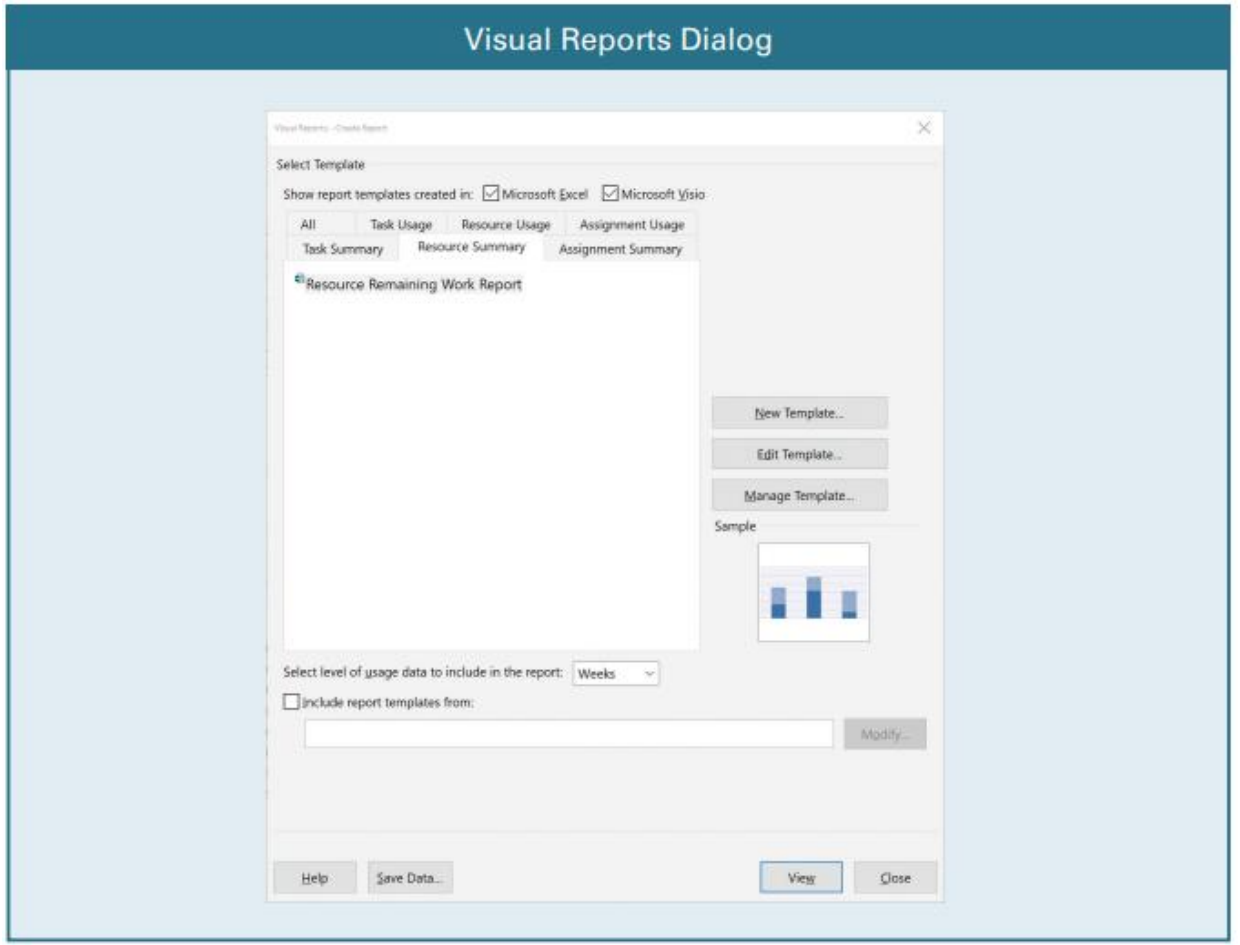

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.7b Archiving Project Work (1 of 3)

STEP 1

Complete the schedule to maximize its future usefulness.

This includes the following:

- Applying performance data.
- Applying approved changes.
- Ensuring all activities are complete.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.7b Archiving Project Work (2 of 3)

STEP 2

Archive the schedule for use as a template or “starter” file.

- Decide the data format—MS Project or a longer-term format.
- Schedule data from the Gantt chart can easily be copied and pasted into applications like MS Excel or Word.
- Decide which baselines to keep *(if there were multiples due to changes)*.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

15.7b Archiving Project Work (3 of 3)

STEP 3

Capture and publish lessons learned about the effectiveness and efficiency of the employed schedule and cost management processes.

Consider retaining items such as the following:

- Frequency and method of team member performance data collection.
- Activity duration maximum and minimum limits.
- Status reporting to Stakeholders.
  - Communication technologies employed and their effectiveness.
  - Schedule and cost estimate accuracy.
  - Max Units value—maximum availability of a resource for work.
  - WBS structure.

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.

Summary

- Projects may be terminated early by: Mutual agreement, Default or Convenience of customer.
- Whether project finishes successfully as planned or not, a variety of closeout procedures is required, including:
  - *Documentation completed and distributed.*
  - *Lessons Learned recorded.*
  - *Money paid and accounted for.*
  - *Workers reassigned and rewarded.*
  - *Success celebrated.*

Kloppenborg | Anantatmula | Wells, Contemporary Project Management: Plan-Driven and Agile Approaches, 5th Edition. © 2023 Cengage.
All Rights Reserved. May not be scanned, copied or duplicated, or posted to a publicly accessible website, in whole or in part.
